



Marina Library Improvement Project

October 28, 2024

Tina Pham
Senior Engineer/Public Works

Agenda

1. Project Background
2. Overview of Project Scope
3. Recent Investigatory Activities
4. Design Development
5. Ongoing Collaboration
6. Anticipated Schedule
7. Funding Overview
8. Next Steps

Project Background

- **Library Location:** 1530 Susan Court
- **Project Goals:**
 - Correct sloping floors and the building's structural issues caused by soil settlement
 - Ensure compliance with ADA standards



Overview of Project Scope




- Structural Foundation Work
- Reconstruction of the Outdoor Deck
- Replacement of Roof and Addition of Roof Insulation
- Replacement of Heating Ventilation & Air Conditioning System (HVAC)
- Replacement of Lighting, Mechanical, & Electrical Building Systems
- Full Interior Renovation

Investigatory Activities

- Building Condition Assessment (Complete)
- Roof Inspection (Complete)
- Helical Pile Testing Field Work (Complete)
- Selective Demolition (In-Progress)
- Concrete Cores Materials Testing (scheduled for November 2025)



Design Development

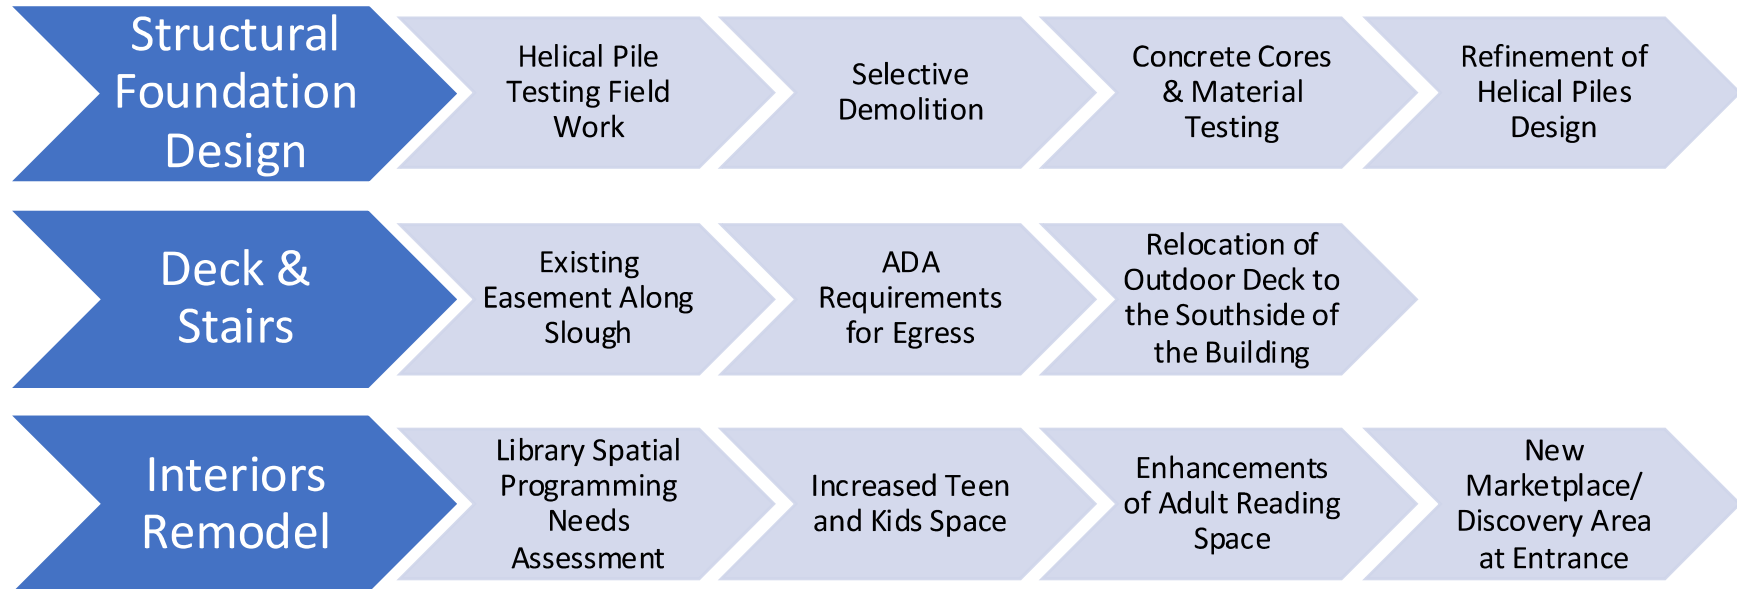






On Going Collaboration

Former Fish Market Site – 1855 S. Norfolk St.

- Current Phase: Planning Application & Environmental Review
- Updated Traffic Impact Analysis (TIA) anticipated by November 2024
- Planning Commission Meeting anticipated by Early 2025
- No tentative construction date yet

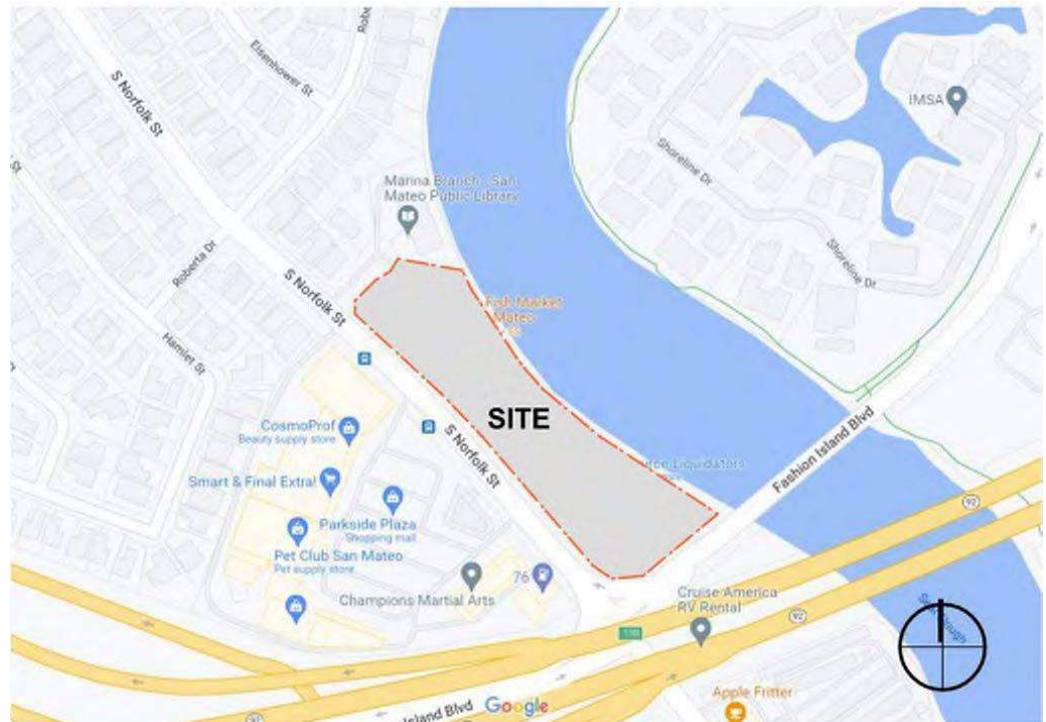

On Going Collaboration

Former Fish Market Site – 1855 S. Norfolk St.

- Design Decisions In-Progress
 - Property gate moved resulting in preserved connection point from Marina Library to café and slough side pathway
 - Trash bins previously proposed on Susan Court changed to compactors and roll off bins stored out of public view






Anticipated Project Schedule

- Pre-design Phase: Complete
- Design Phase: Current Phase – Spring 2025
- Bid & Award Phase: April – May 2025
- Construction Phase: Summer 2025 – Summer 2026



Funding Overview

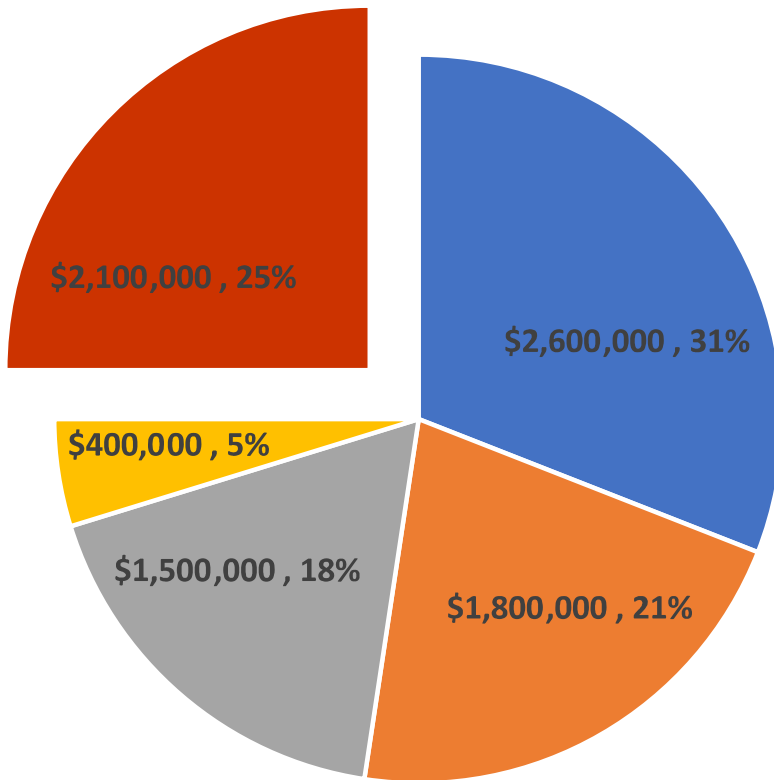

- Local Funding - Measure S & General Fund (\$2.6 Million)
- California State Library Grant Funding (\$1.8 Million)
- Federal HUD Grant (\$1.5 Million)
- Potential Funding for HVAC Efficiency Improvements (\$0.4 Million)
- Funding Gap (\$2.1 Million)

• Total Funding Need: \$8,300,000

Next Steps

- Environmental Review Process complete by end of 2024
- Design completed by Spring 2025
- Funding Gap Analysis and Securing Additional Funds





Thank You

Tina Pham

Senior Engineer

tpham@cityofsanmateo.org

www.cityofsanmateo.org/publicworks
